






Drumul critic

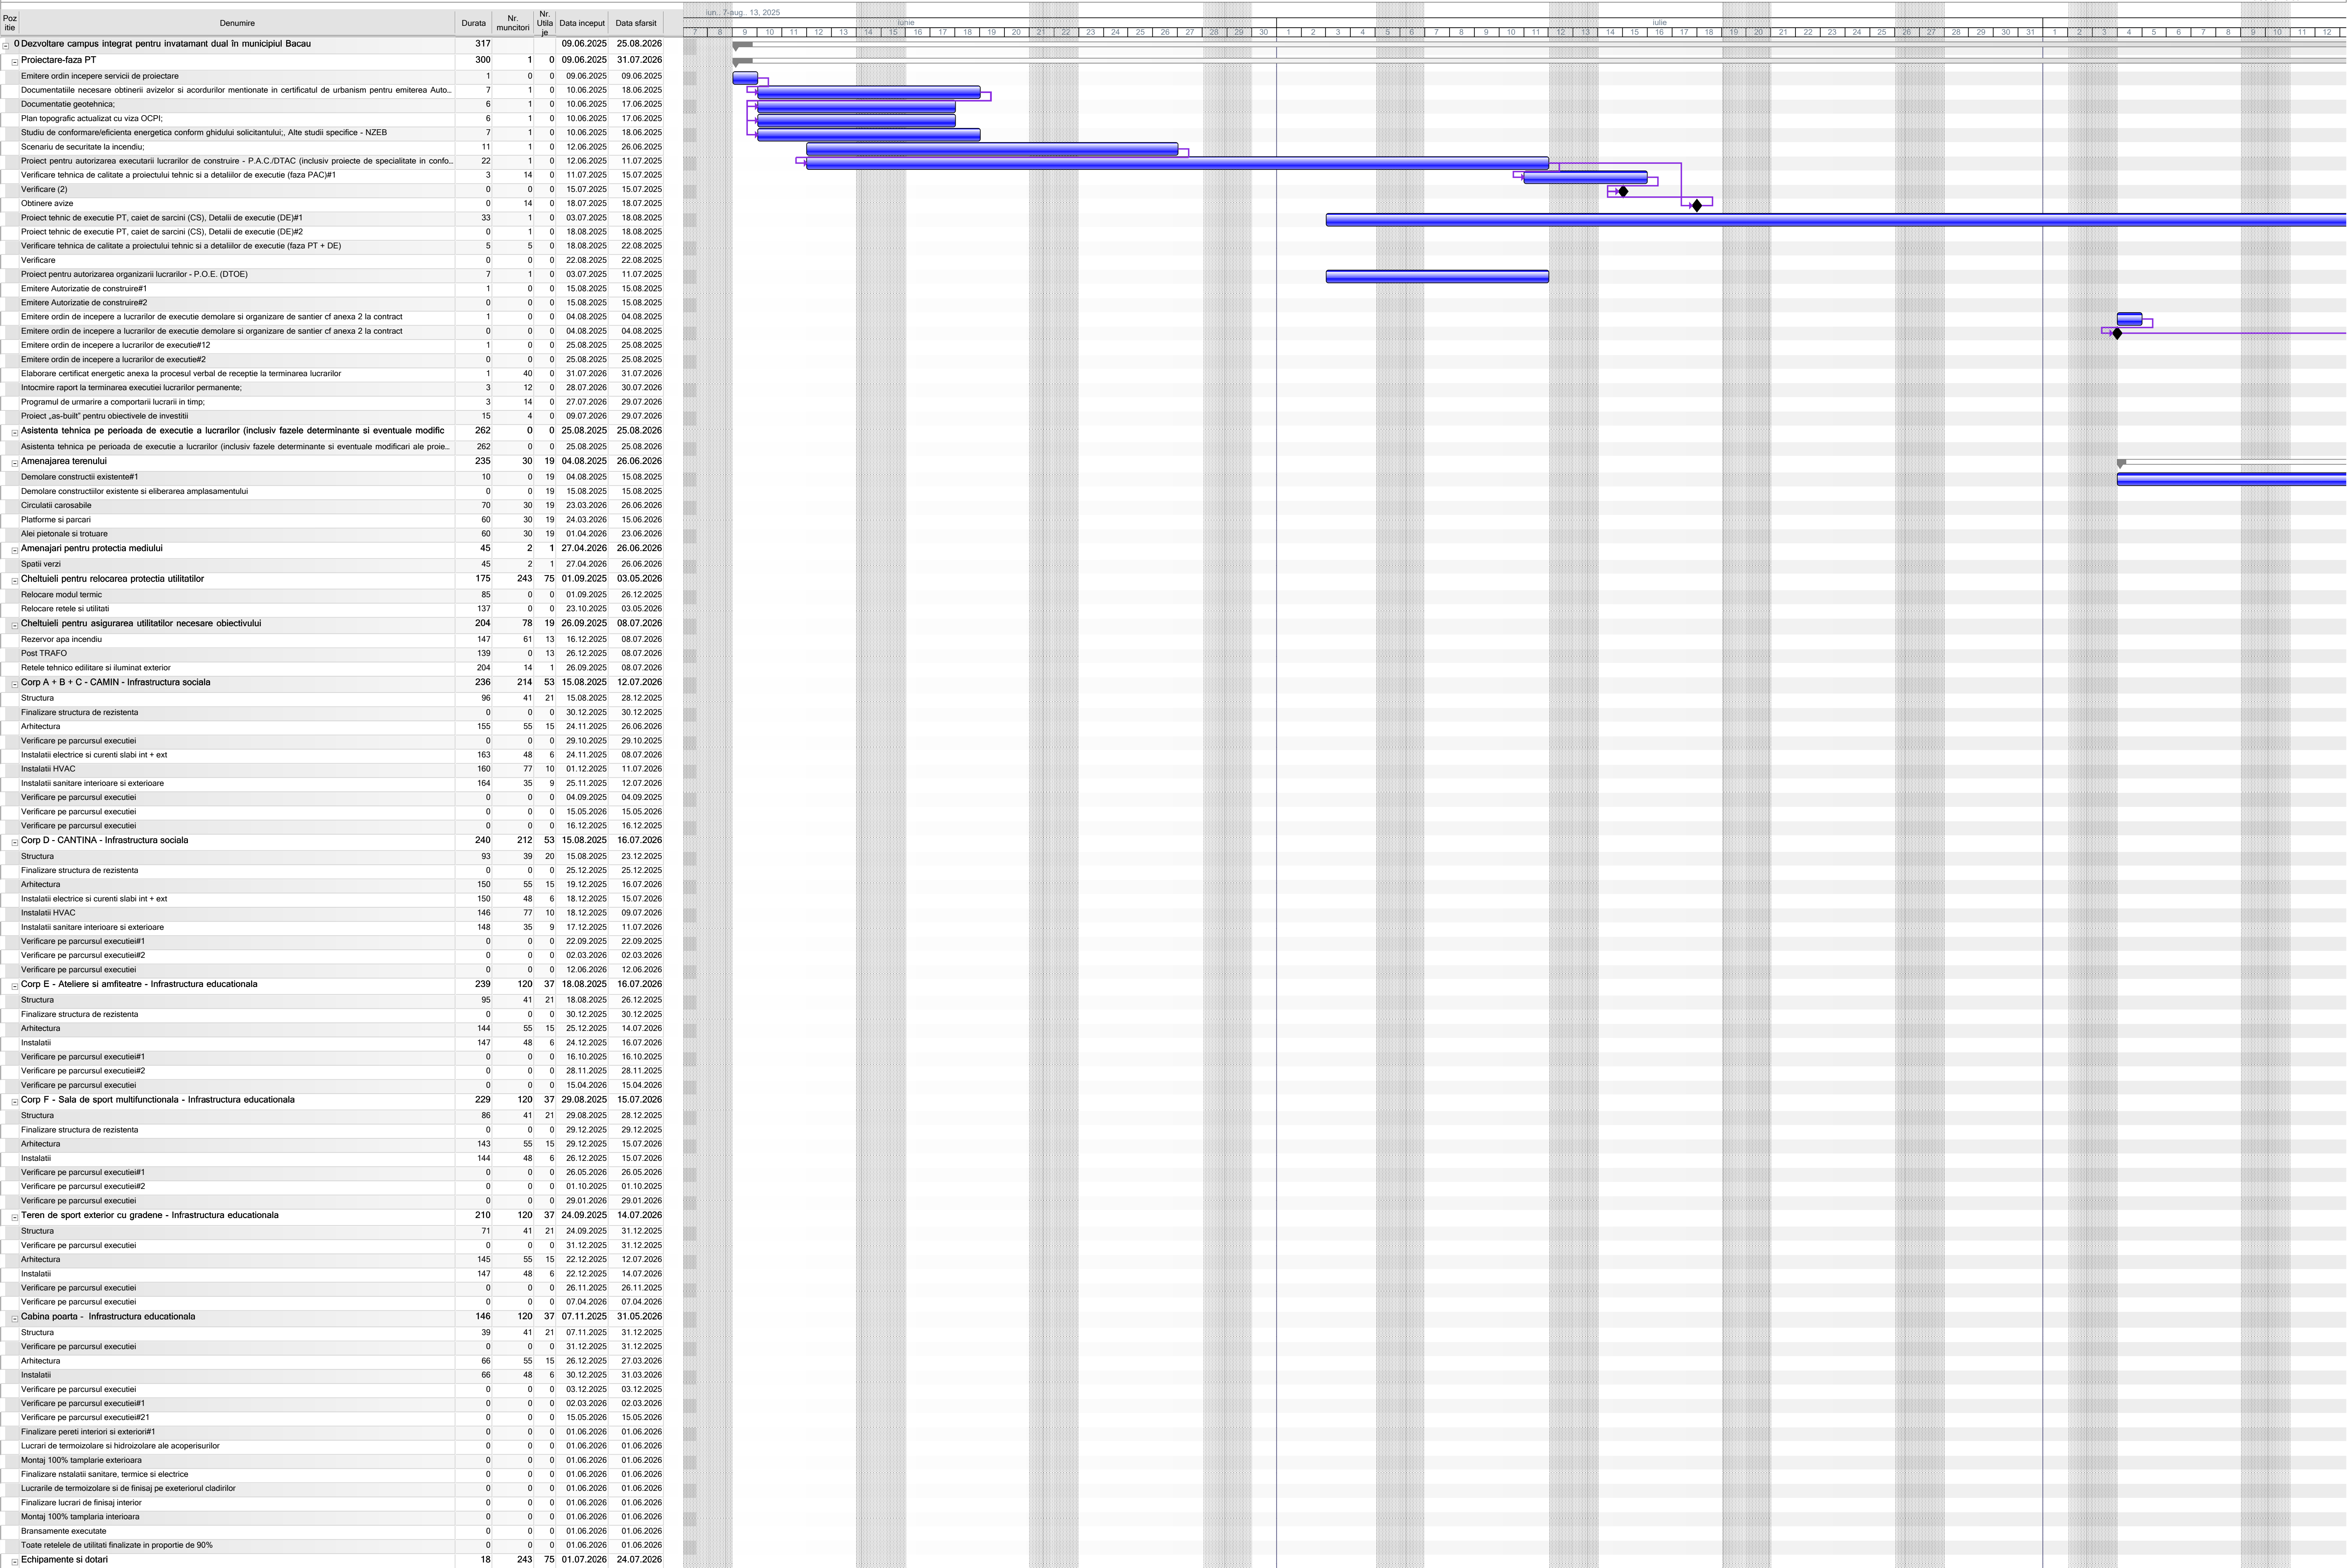



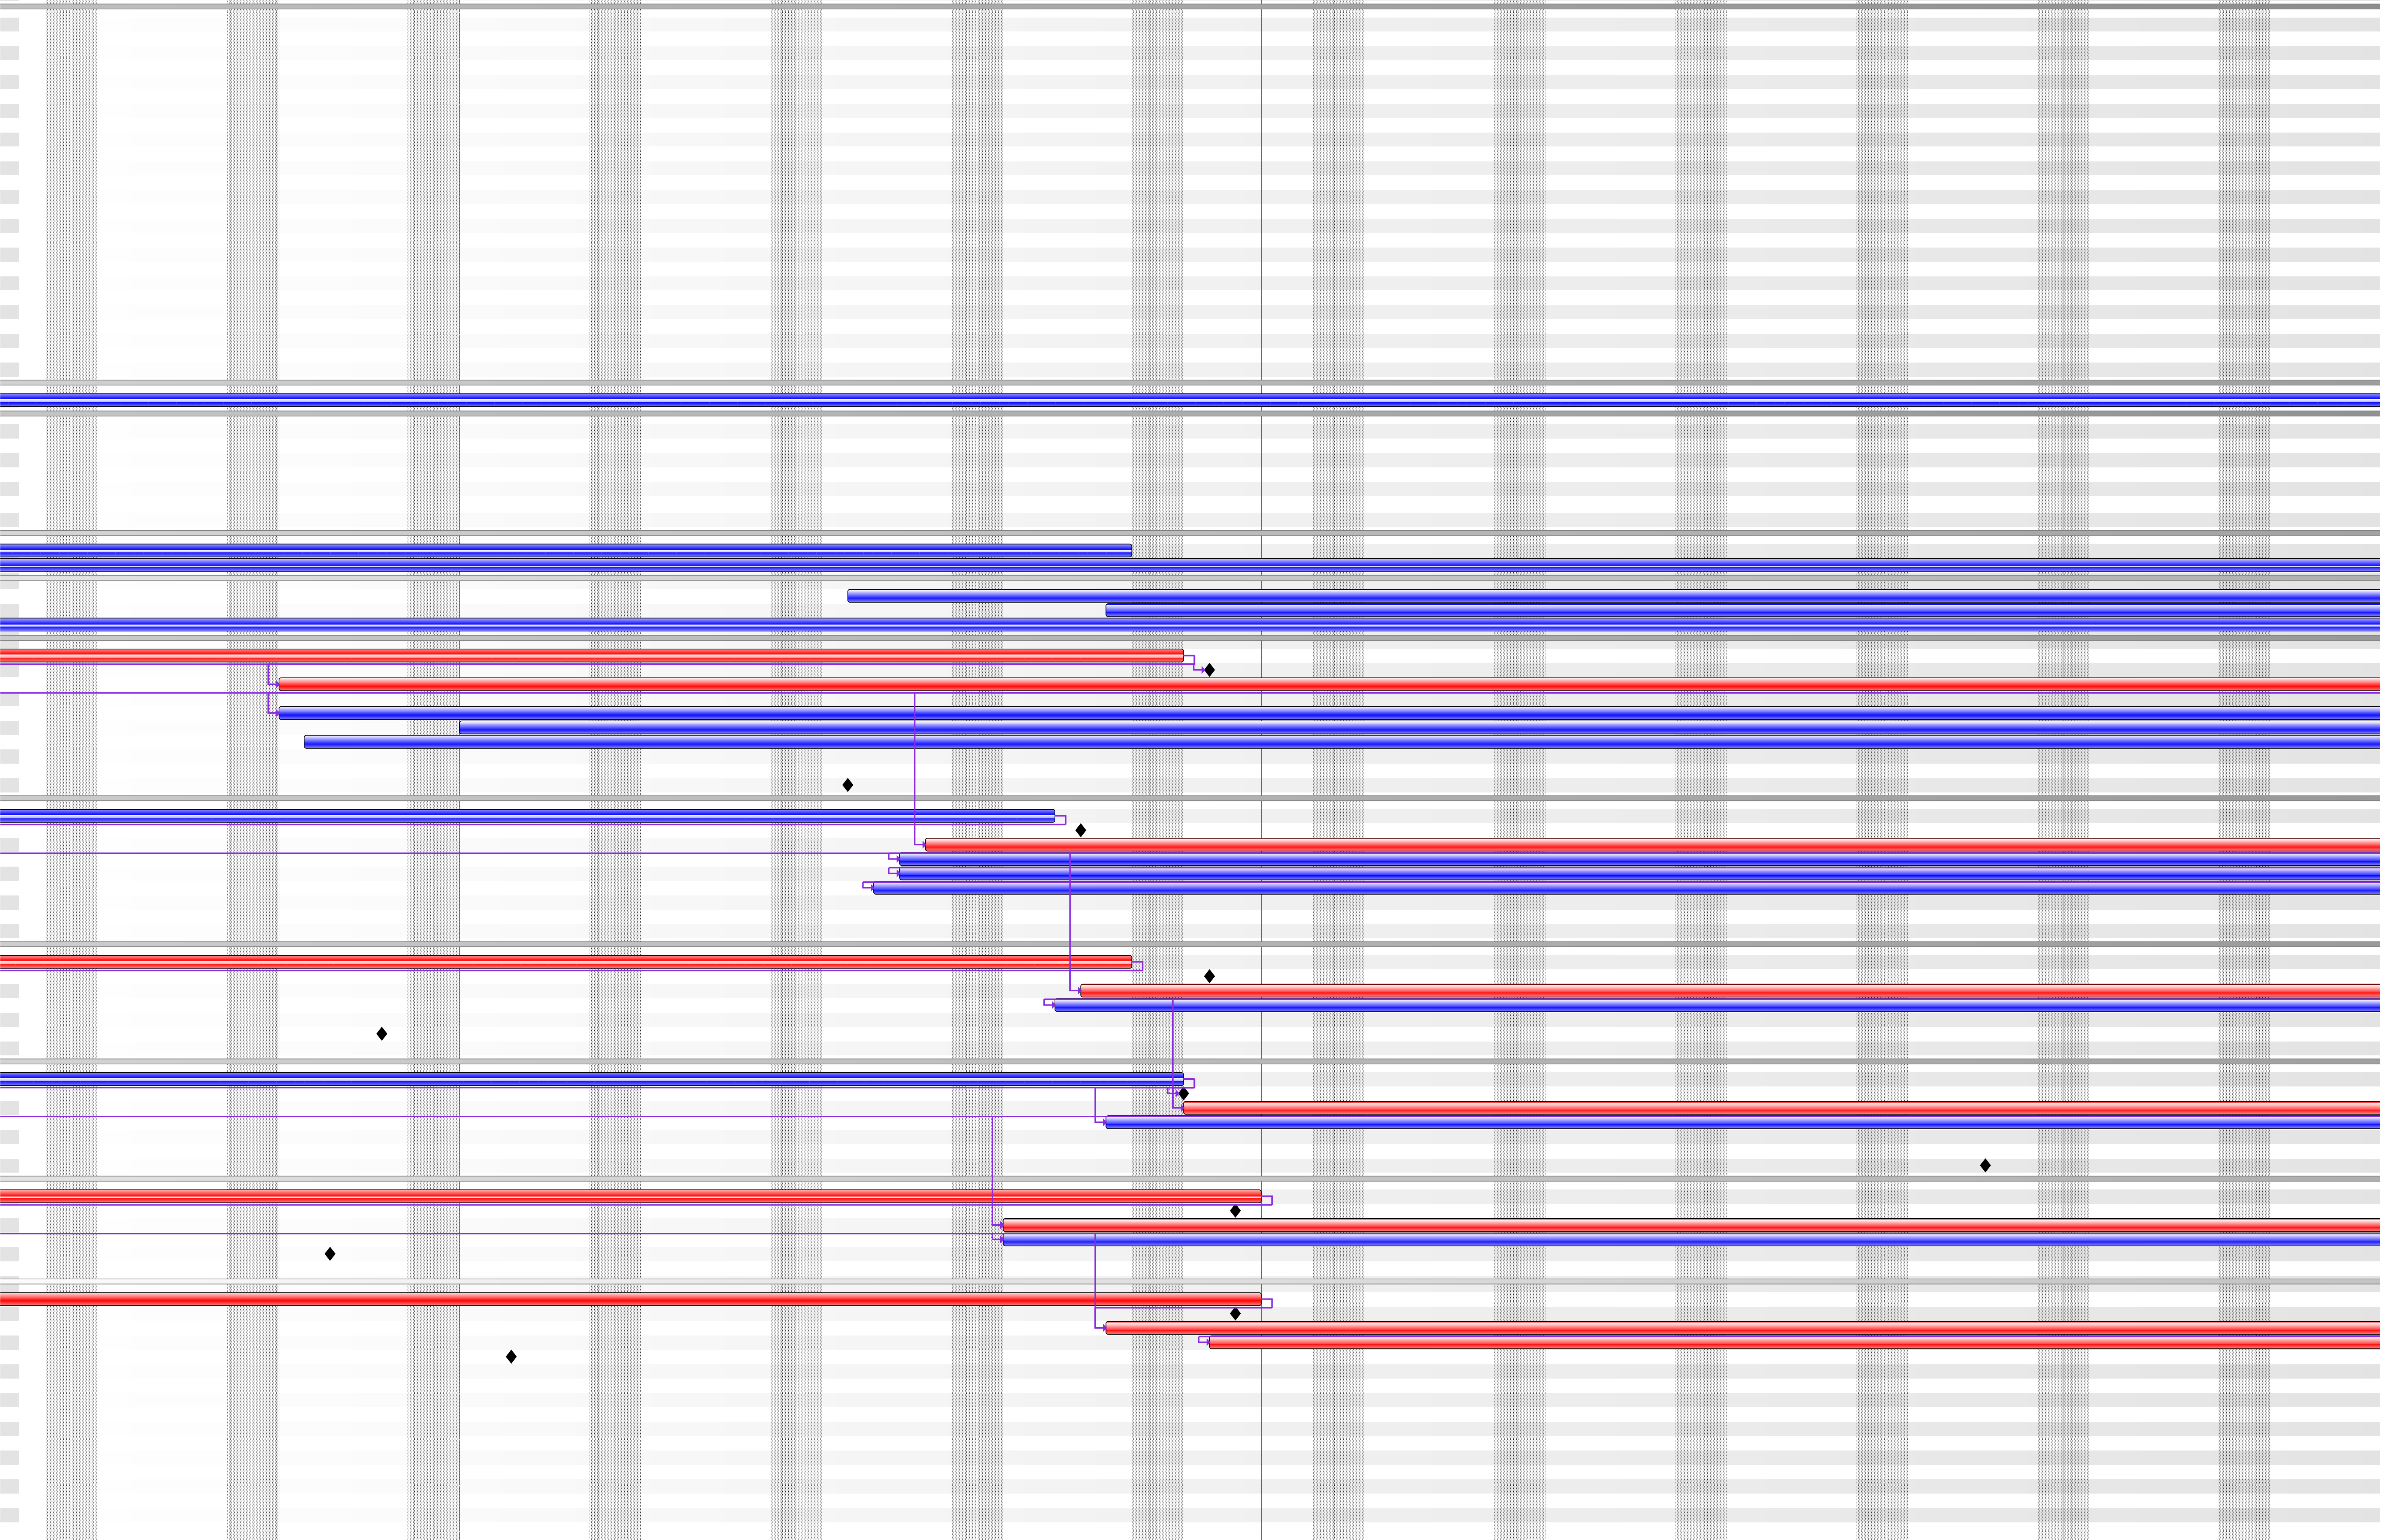

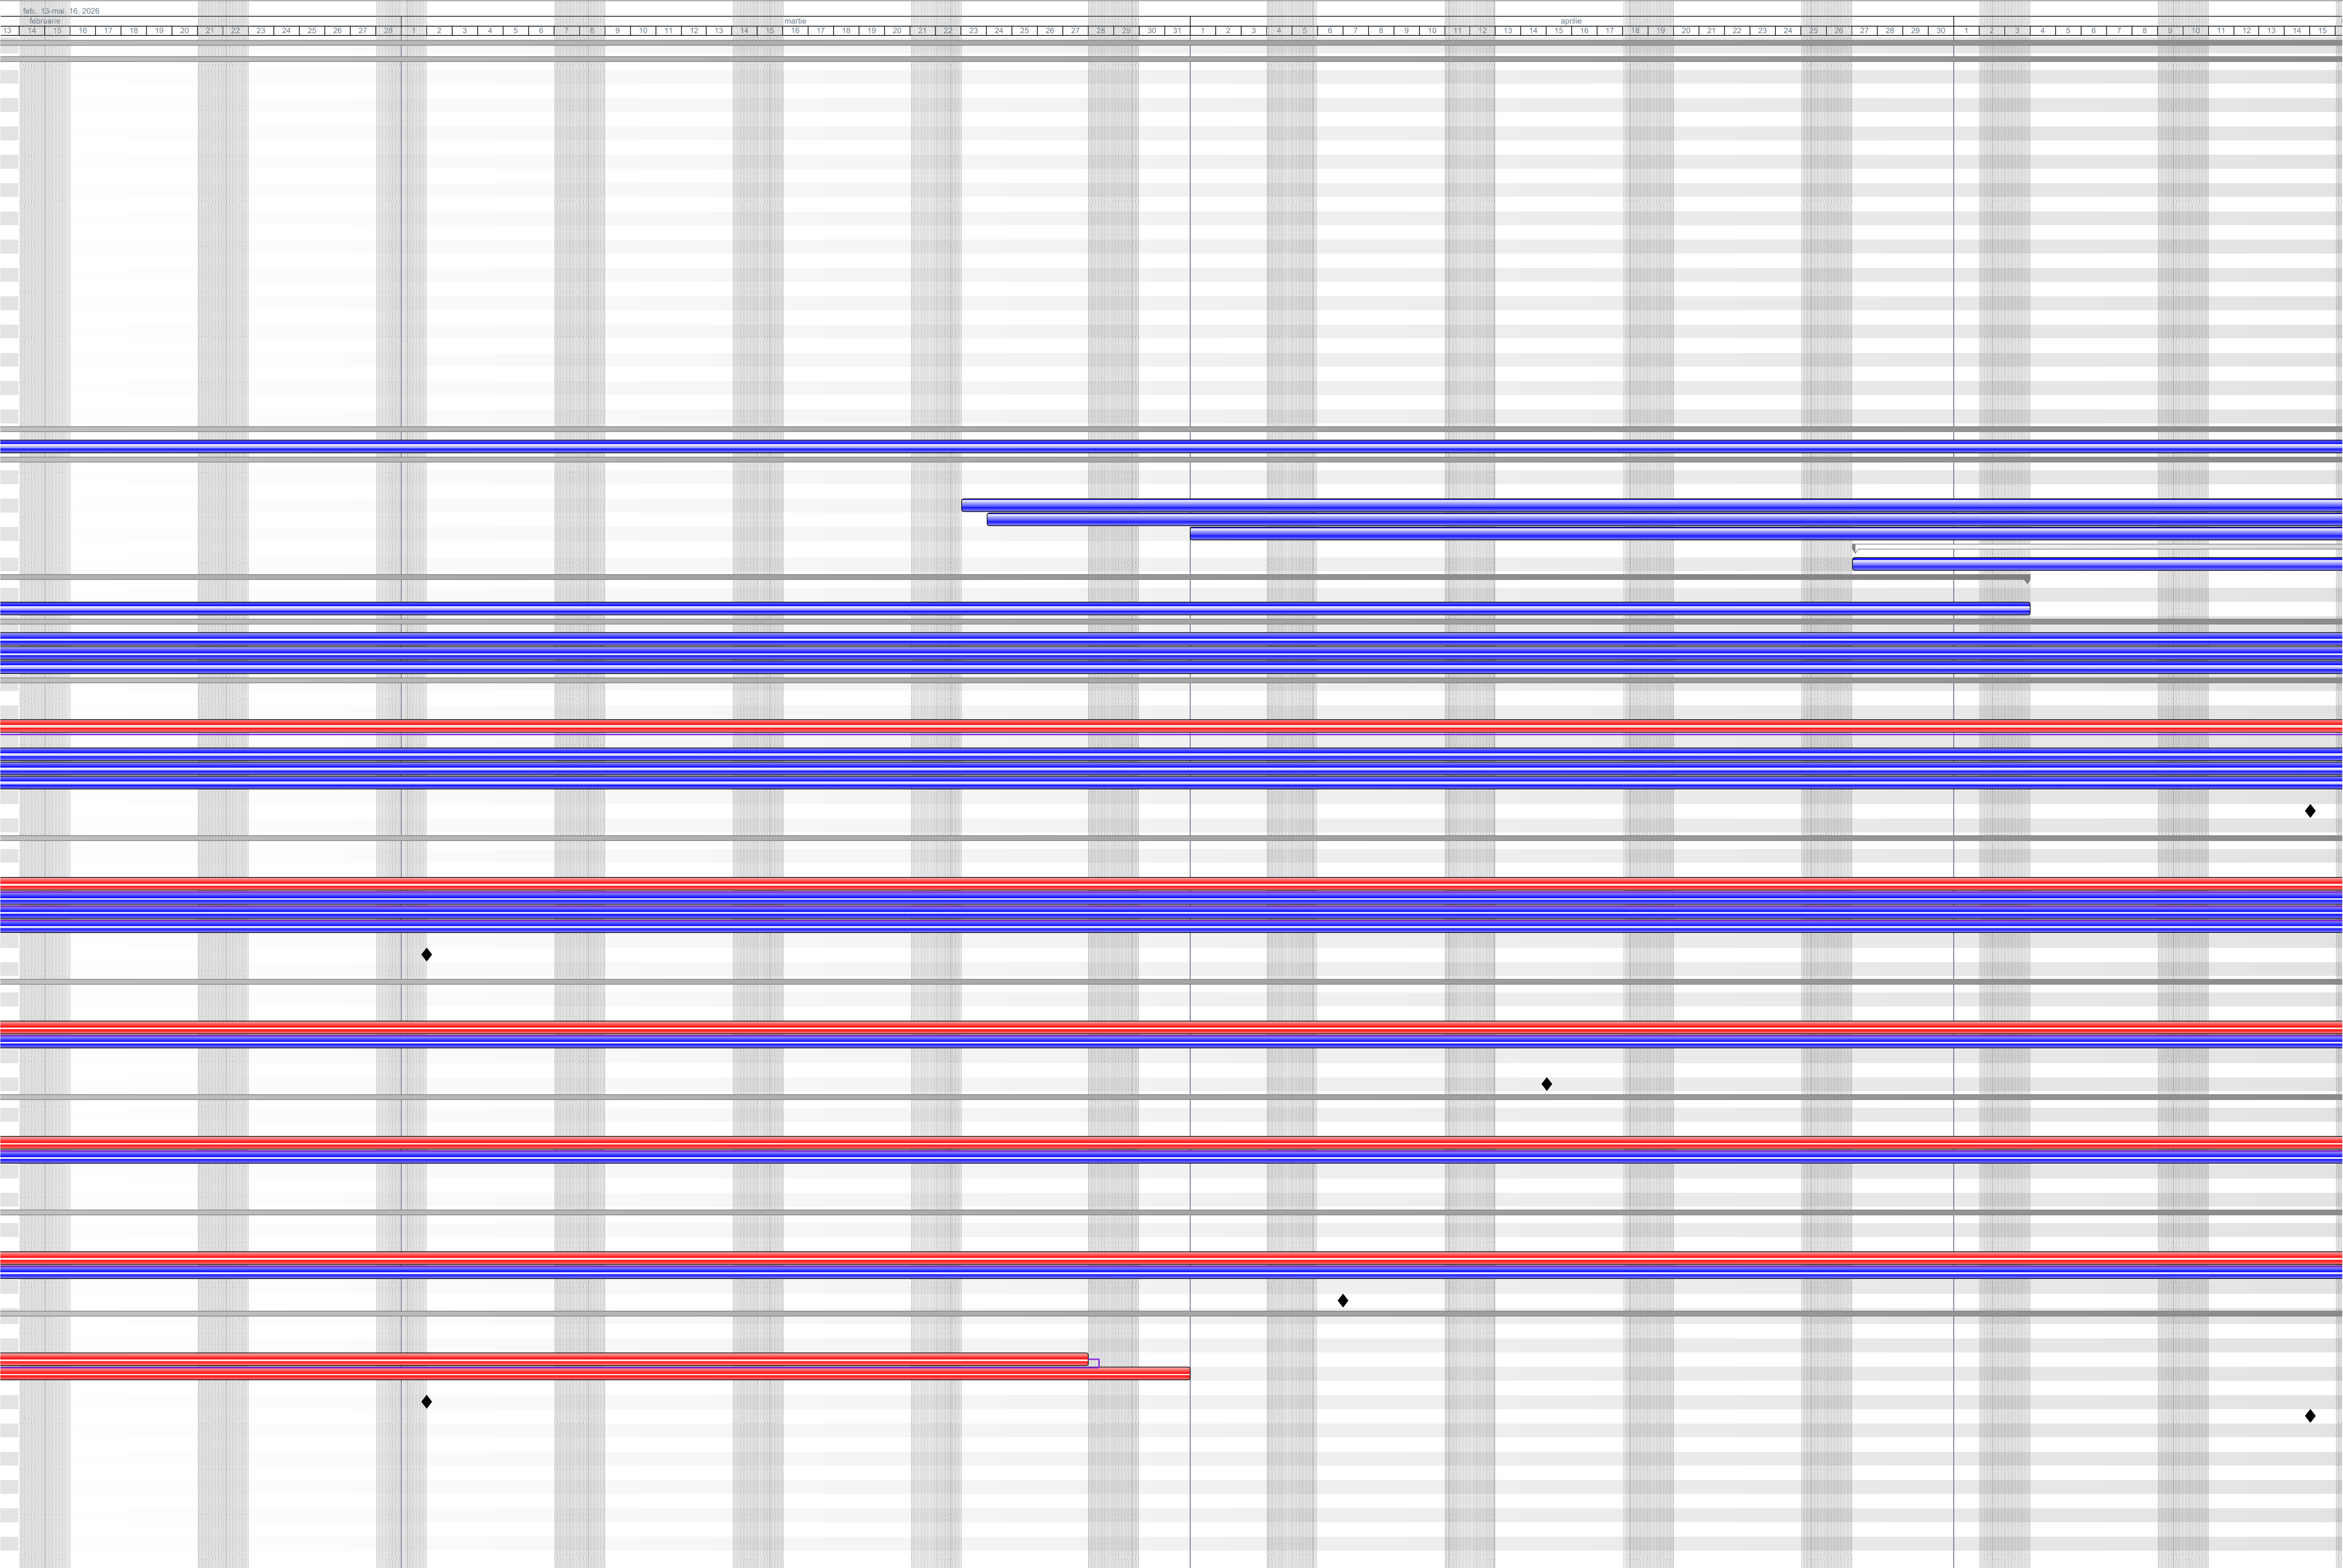

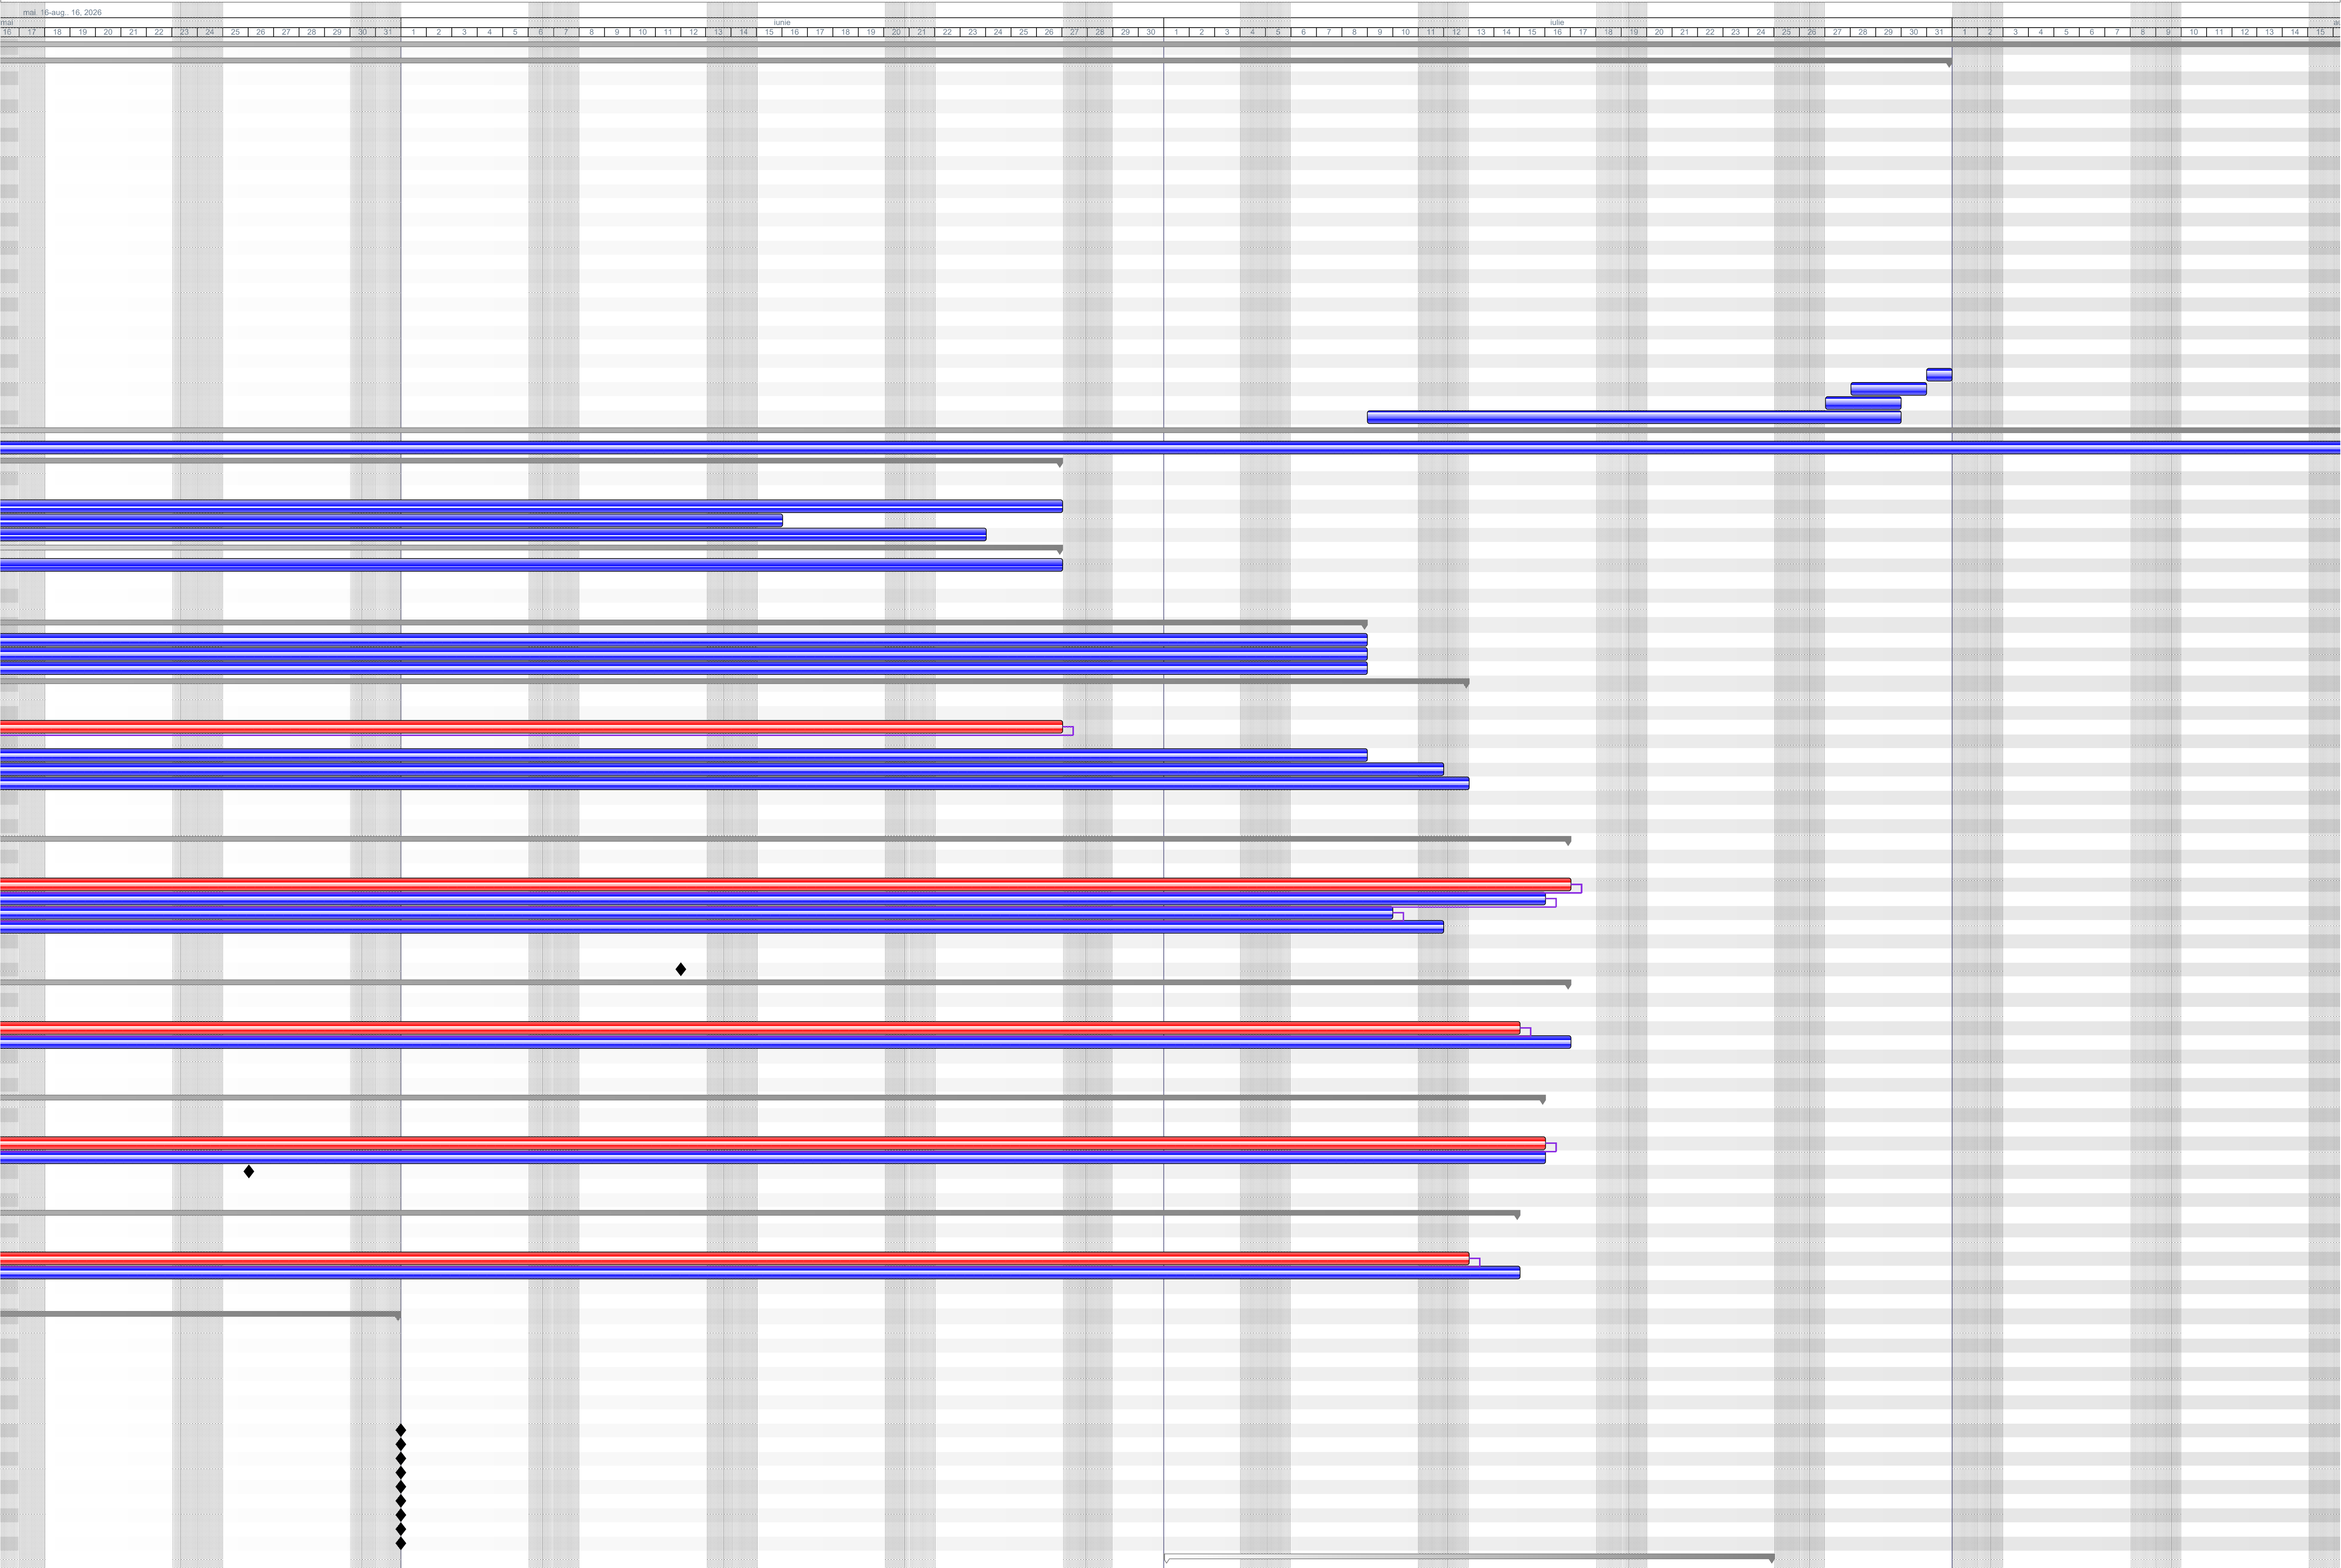

14 Echipamente#1	18	0	0	01.07.2026	24.07.2026
Dotarea tuturor cladirilor, dotarea curtilor si calilor de acces	0	0	0	24.07.2026	24.07.2026
05 Organizare de santier	260	6	4	04.08.2025	31.07.2026
01 Organizare de santier#1	10	0	6	04.08.2025	15.08.2025
01 Organizare de santier#2	0	0	6	15.08.2025	15.08.2025
Cheltuieli conexe organizarea de santier	246	0	0	15.08.2025	24.07.2026
Mentinere OS	247	0	0	15.08.2025	27.07.2026
Desfiintare OS	4	0	0	28.07.2026	31.07.2026
Receptie la terminarea lucrarilor	17			03.08.2026	25.08.2026
Receptie la terminarea lucrarilor (inclusiv predarea cartii tehnice a constructiei)	17	0	0	03.08.2026	25.08.2026
Semnare P.V.R.T.L.#1	6	0	0	18.08.2026	25.08.2026
Semnare P.V.R.T.L.#2	0	0	0	25.08.2026	25.08.2026

